

L.J. COPPOLA INC.

MECHANICAL CONTRACTORS

40 Farrington Road
Brewster, NY 10509
(914) 769-7666
Fax: (914) 769-5141
Plumbing License No. 750

PLUMBING

H.V.A.C.

PROCESS PIPING

SEWAGE TREATMENT

ESTABLISHED 1972

REQUEST FOR INFORMATION

Project: HARRISON REC CENTER PHASE 2 **Date:** 11/19/24 **Log No.:** LJC# -03

Drwg.: P401 **Spec.:** N/A **Area:** LOCKER ROOM

Directed To: Piazza Brothers **Date Required:**

Impact: N/A

Regarding: SHOWER INSTALLATION

REQUESTED BY: S. MCCABE/P. DOLSON **cc:**

INFORMATION REQUIRED:

The water closet in the ADA stall in room 116, women's locker room, is shown directly above a pier and adjacent to structural steel. The carrier and drain piping will not fit, therefore, is it acceptable to mirror the ADA stall as per the attached drawing?


IT IS ACCEPTABLE TO FLIP THE WATER CLOSET TO THE NORTH SIDE OF THE STALL TO AVOID THE STEEL AND PIER. GC TO COORD THE DOOR SWING OF THE TOILET PARTITION AND ASSOCIATED GRAB BARS THAT WILL BE RELOCATED WITH THE TOILET

RESPONSE:

RESPONSE BY:

RESPONSE DATE: **cc:**

Your response is requested by the date listed above. Failure to respond by this date may delay the project schedule and may have a cost impact.

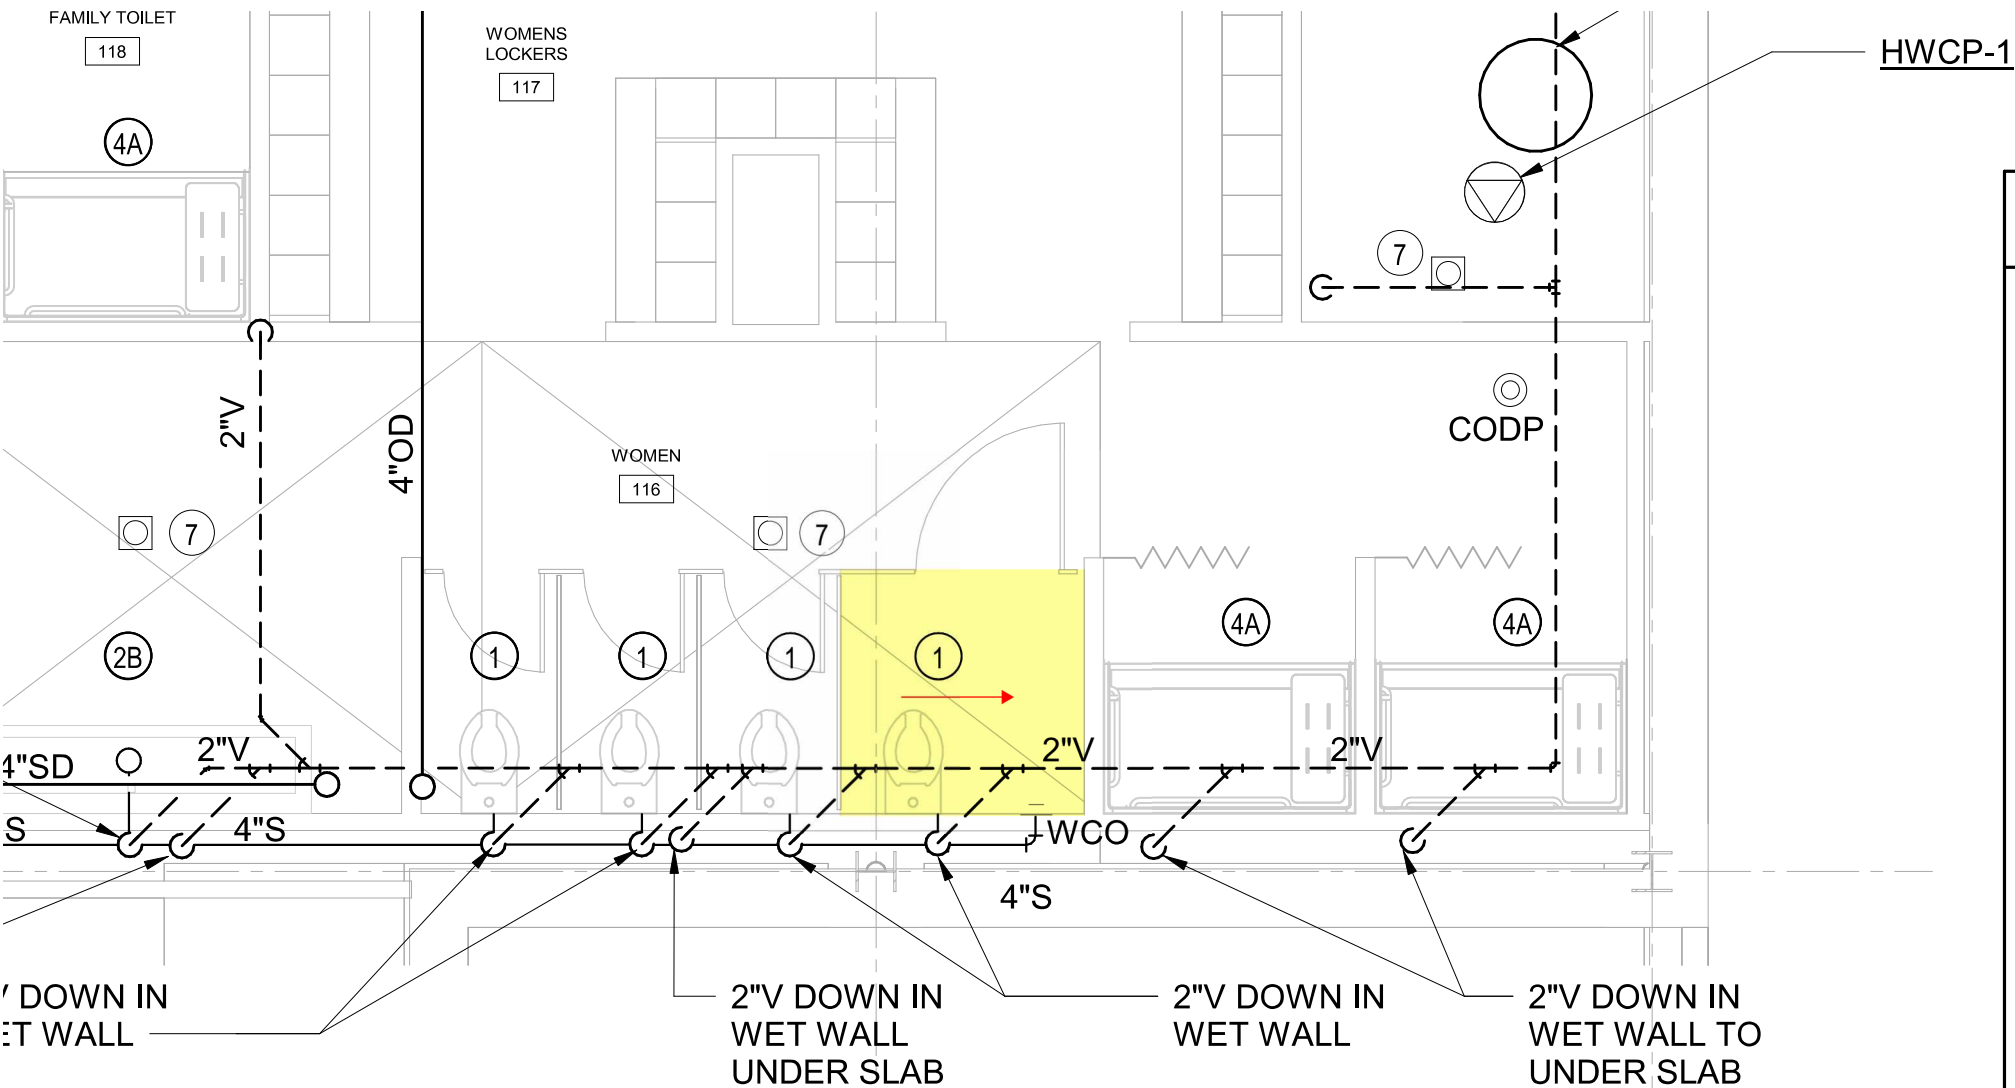

BING FIRST FLOOR LOCKER ROOMS - SANITARY PLAN

' = 1'-0"

NE

1

2

2A

2B

3

4

4A

5

5A

6

7

